

Planning

Design

Construction

Complete

Projected Construction Phases: NE 85th Street Corridor Improvements

Construction phases will be staggered to minimize traffic congestion and reduce construction impacts.

311

385

濉

Phase I

Intersection Improvements

- √ COMPLETE: Install additional southbound 114th Ave NE to eastbound NE 85th St left turn lane. Upgrade traffic signal controller equipment to connect to new computer network for remote monitoring and control.
- Add traffic island at NE 124th Ave NE for future eastbound to northbound turn lane.
 Upgrade traffic signal controller equipment to connect to new computer network for remote monitoring and control.
- Add northbound 132nd Ave to eastbound NE 85th St right turn lane. Upgrade traffic signal controller equipment to connect to new computer network for remote monitoring and control.

Phase 2

Undergrounding Utility Wires

- IN PROGRESS: Underground utility wires along NE 85th St from 120th Ave NE to
- IN PROGRESS: Install conduit for future undergrounding of utility wires along NE 85th St from 128th Ave NE to 132nd Ave NE.


Phase 3

Sidewalks with landscape planter strips where there are none

- Install sidewalks (where there are none) on both sides of 124th Ave NE between NE 80th St and NE 90th St. Include landscaped planter strips between road and sidewalk where possible.
- Install sidewalk (where there are none) on both sides of NE 85th St between 120th Ave NE and 132nd Ave NE. Include landscaped planter strips with trees between road and sidewalk where possible. Install energy efficient street lighting.

Resurface Street

 Preserve the City's infrastructure and reduce costly repairs by overlaying entire NE 85th St Corridor from 114th Ave NE to 132nd Ave NE.

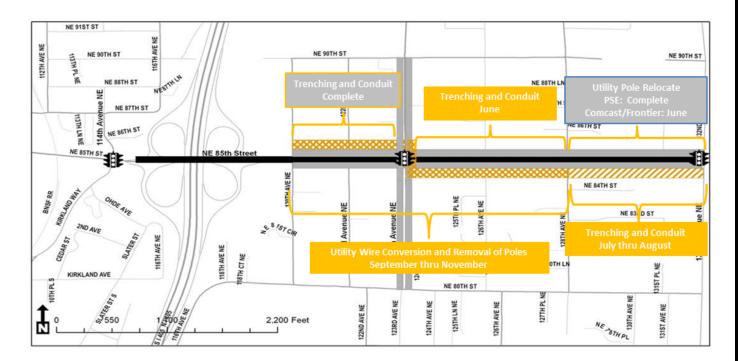



NE 85th STREET CORRIDOR IMPROVEMENTS PROJECT



Project Update June 22, 2012

Transforming NE 85th Street into a safer, more efficient, and pedestrian-friendly corridor.

What: Thank you for your patience as the NE 85th Street Corridor Improvements are being made. The City of Kirkland, and it's contractor Tri State Construction, are undergrounding overhead utility wires on NE 85th Street from 120th Avenue NE to 128th Avenue NE. In addition, they will be installing underground conduit for future wire undergrounding from 128th Avenue NE to 132nd Avenue NE.

When: Construction began in late February and is anticipated to be complete by November 2012. Daytime work hours are scheduled between 7:00am and 3:30pm. Some night work may be necessary to avoid traffic impacts. All work is weather-dependent and could be rescheduled due to inclement weather.

COMPLETE


- √ Conduct preconstruction surveying the length of the corridor and explore various pavement depths and utility locations prior to trenching.
- √ Install large electrical vaults into the ground at various locations along the corridor. (PSE request for one additional at Walgreens by end of June).
- √ Trench and install conduit on the north side of NE 85th Street from 120th to 124th Avenue NE. (Property restoration to be complete end of June).
- √ Trench and install conduits on 120th Avenue NE and complete storm drainage modifications at this location. (Property restoration to be complete end of June).
- Relocate utility poles on the south side of NE 85th Street between 128th Avenue NE and 132nd Avenue NE in preparation for conduit to be installed. (PSE complete, Comcast to be done by June 4th, Frontier to be done by June 28th).
- √ Trench and install conduit along south side of NE 85th Street from 124th Avenue NE to 128th Avenue NE. (Nearing completion end of June.)

UPCOMING

- July-August: Trench and install conduit for future undergrounding on the south side of NE 85th Street from 128th Avenue NE to 132nd Avenue NE as well as across NE 85th Street at 132nd Avenue NE.
- September November: Run new wires within conduit and begin using underground wires between 122nd Avenue NE and 128th Avenue NE. Remove poles.
- Fall: Complete private underground connections from City right of way to private property.

What to expect: One lane of traffic may be closed intermittently where necessary. Flagging operations will be in effect directing traffic as needed. No-parking signs will be posted at least 24 hours in advance of any parking restrictions. Open trenches will be backfilled and/or covered at the end of each work day. Emergency vehicle access will be maintained throughout the construction process.

Thank you for your patience and cooperation as we make improvements to this important corridor.



Stay Informed and Involved

Access up to date information:
Go to www.kirklandwa.gov/85th Street.

Call the construction hotline: (425) 587-3838.

Sign up for email updates: Go to www.kirklandwa.gov/85thStreet and click on this symbol.



Join the Construction Advisory Group (CAG): for businesses along NE 85th Street Corridor to stay involved in construction impacts and options for mitigation. All are welcome to attend.

The next Construction Advisory Group meeting will be:

July 9, 2012 10:00 am Honda of Kirkland 12420 Northeast 85th Street

Contact: Kari Page, Neighborhood Outreach Coordinator at KPage@kirklandwa.gov or 425-587-3011
